

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Name: HARSHITH R SRN: PES1UG24AM117

Scenario: Telemedicine Slot Booking & Prescription Portal

My part: Set 3, Tele-Consultation Session (UC-04 and UC-05)

1. Introduction

In Lab 1 our team of four wrote the requirements for a telemedicine portal and split the work into four sets. For this lab I used only my own set, Set 3, so my Epic and User Stories are different from my teammates'. I took the requirements for generating the encrypted video consultation link (FR-004), the UC-04 and UC-05 flow, and the connection-drop case, and turned them into an Epic and User Stories in Jira. Then I estimated them, prioritised them and ran two sprints.

Jira project: Telemedicine-Booking (key MP), Scrum template.

2. Epic

Epic	Epic Description
MP-1 Epic 1: Tele-Consultation Session	Enables patients and attending physicians to conduct a secure tele-consultation using a single-use encrypted video link, with session tracking and encrypted clinical notes. (UC-04, UC-05)

The screenshot shows the Jira web interface for the 'HTL board'. The left sidebar contains navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Recent', 'Har-Tele', 'HTL board', 'More spaces', 'Recommended', 'Create a roadmap', 'Filters', 'Dashboards', 'Assets', 'Teams', 'Goals', 'Projects', and 'Customize sidebar'. The main content area has a search bar and a 'Create' button. Below the search bar, there's a 'Summary' tab and a 'Timeline' tab. The 'Active sprints' tab is selected, showing 'HTL Sprint 1' with '0 work items'. The 'Backlog' tab is also visible, showing '0 work items'. A modal window is open for the 'Epic' 'Tele-Consultation Session' with details like 'Key: HTL-1', 'Work Items: 0', 'Completed: 0', and 'Estimate: 0 points'. The modal also has buttons for 'View details', 'Create work item', and 'Create epic'.

3. User Stories, Priority and Story Points

Every story is written as “As a patient/physician, I want ..., so that ...” in the description in Jira. Story points use the Fibonacci scale. The eight stories add up to 40 points in total.

Key	Story	Priority	Points
MP-2	Story 1.1: Generate Encrypted Video Consultation Link	High	5
MP-3	Story 1.2: Validate Consultation Link and Appointment Window	High	3
MP-4	Story 1.3: Admit Patient to Virtual Waiting Room	Medium	3
MP-5	Story 1.4: Conduct Secure Video Consultation	High	8
MP-6	Story 1.5: Record Clinical Notes During Consultation	High	5
MP-7	Story 1.6: Record Consultation Completion and Duration	Medium	3
MP-8	Story 1.7: Handle Connection Drop and Reconnection	High	8
MP-9	Story 1.8: Complete Consultation and Enable Prescription Authoring	Medium	5

Spaces / Har-Tele

HTL board

SummaryTimelineActive sprintsBacklogCalendarListFormsDevelopmentDocs

Search backlogHRVersionEpic 1Quick filtersClear filters

Epic

No epic

Tele-Consultation Session

KeyHTL-1

Work items8

Completed0

Estimate40 points

0% of estimated work complete

0 work items unestimated

View details

Create work item

Create epic

Backlog (8 work items)

4000Create sprint

Create a whiteboard to plan your workTry

HTL-2STORY-1: Generate Encrypted Video Consultati...Tele-Con...To Do5

HTL-3STORY-2: Validate Consultation Link and Appoi...Tele-Con...To Do3

HTL-4STORY-3: Admit Patient to Virtual Waiting RoomTele-Con...To Do3

HTL-5STORY-4: Conduct Secure Video ConsultationTele-Con...To Do8

HTL-6STORY-5: Record Clinical Notes During Consult...Tele-Con...To Do5

HTL-7STORY-6: Record Consultation Completion and ...Tele-Con...To Do3

HTL-8STORY-7: Handle Connection Drop and Reconn...Tele-Con...To Do8

HTL-9STORY-8: Complete Consultation and Enable Pr...Tele-Con...To Do5

Create

4. Sprints

I put the stories into two sprints. Sprint 1 had the first five consultation stories (24 points). The second sprint had the remaining three stories, including reconnection and completion/prescription handoff (16 points). Each sprint was started and the stories were moved from To Do to In Progress to Done one by one as a simulation.

Sprint	Stories	Points	Goal
MP Sprint 1	MP-2, 3, 4, 5, 6	24	Securely start and conduct the tele-consultation and record clinical notes
MP Sprint 2	MP-7, 8, 9	16	Complete the session reliably, handle reconnection, and enable the next prescription step

SPRINT-1 : PLANNING

Spaces / Har-Tele

HTL board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

+

Search backlog

HR

Version

Epic 1

Quick filters

Clear filters

Epic

No epic

Tele-Consultation Session

Key HTL-1

Work items 8

Completed 0

Estimate 40 points

0% of estimated work complete

0 work items unestimated

HTL Sprint 1

Add dates

(5 work items)

24 0 0

Start sprint

HTL-2

STORY-1: Generate Encrypted Video Consultati...

Tele-Con...

To Do

5

HTL-3

STORY-2: Validate Consultation Link and Appoi...

Tele-Con...

To Do

3

HTL-4

STORY-3: Admit Patient to Virtual Waiting Room

Tele-Con...

To Do

3

HTL-5

STORY-4: Conduct Secure Video Consultation

Tele-Con...

To Do

8

HTL-6

STORY-5: Record Clinical Notes During Consult...

Tele-Con...

To Do

5

+ Create

5 of 5 work items visible

Estimate: 24 of 24

ACTIVE SPRINT : 1

Spaces / Har-Tele

HTL board

Summary Timeline **Active sprints** Backlog Calendar List Forms Development Docs +

Search board HR Version Epic Quick filters Complete sprint Group: Story

TO DO 5

- STORY-1: Generate Encrypted Video Consultation Link
Tele-Consultation Session
HTL-2 5
- STORY-2: Validate Consultation Link and Appointment Window
Tele-Consultation Session
HTL-3 3
- STORY-3: Admit Patient to Virtual Waiting Room
Tele-Consultation Session
HTL-4 3
- STORY-4: Conduct Secure Video Consultation
Tele-Consultation Session
HTL-5 8
- STORY-5: Record Clinical Notes During Consultation

IN PROGRESS

+ Create

DONE

ONGOING SPRINT-1

Spaces / Har-Tele

HTL board

Summary Timeline **Active sprints** Backlog Calendar List Forms Development Docs +

Search board HR Version Epic Quick filters Complete sprint Group: Story

TO DO 3

- STORY-3: Admit Patient to Virtual Waiting Room
Tele-Consultation Session
HTL-4 3
- STORY-4: Conduct Secure Video Consultation
Tele-Consultation Session
HTL-5 8
- STORY-5: Record Clinical Notes During Consultation
Tele-Consultation Session
HTL-6 5


IN PROGRESS 2

- STORY-1: Generate Encrypted Video Consultation Link
Tele-Consultation Session
HTL-2 5
- STORY-2: Validate Consultation Link and Appointment Window
Tele-Consultation Session
HTL-3 3


DONE

+ Create


COMPLETED SPRINT-1

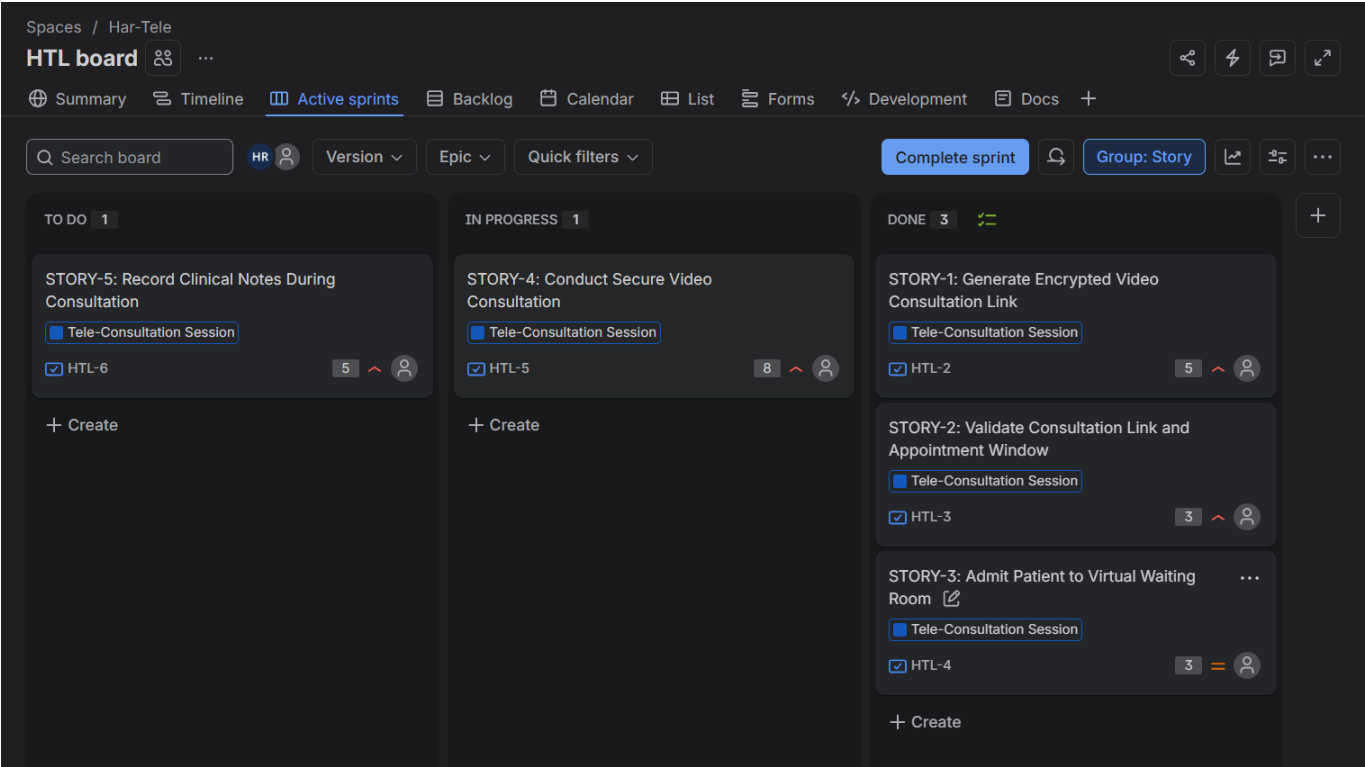

ACTIVE SPRINT-2

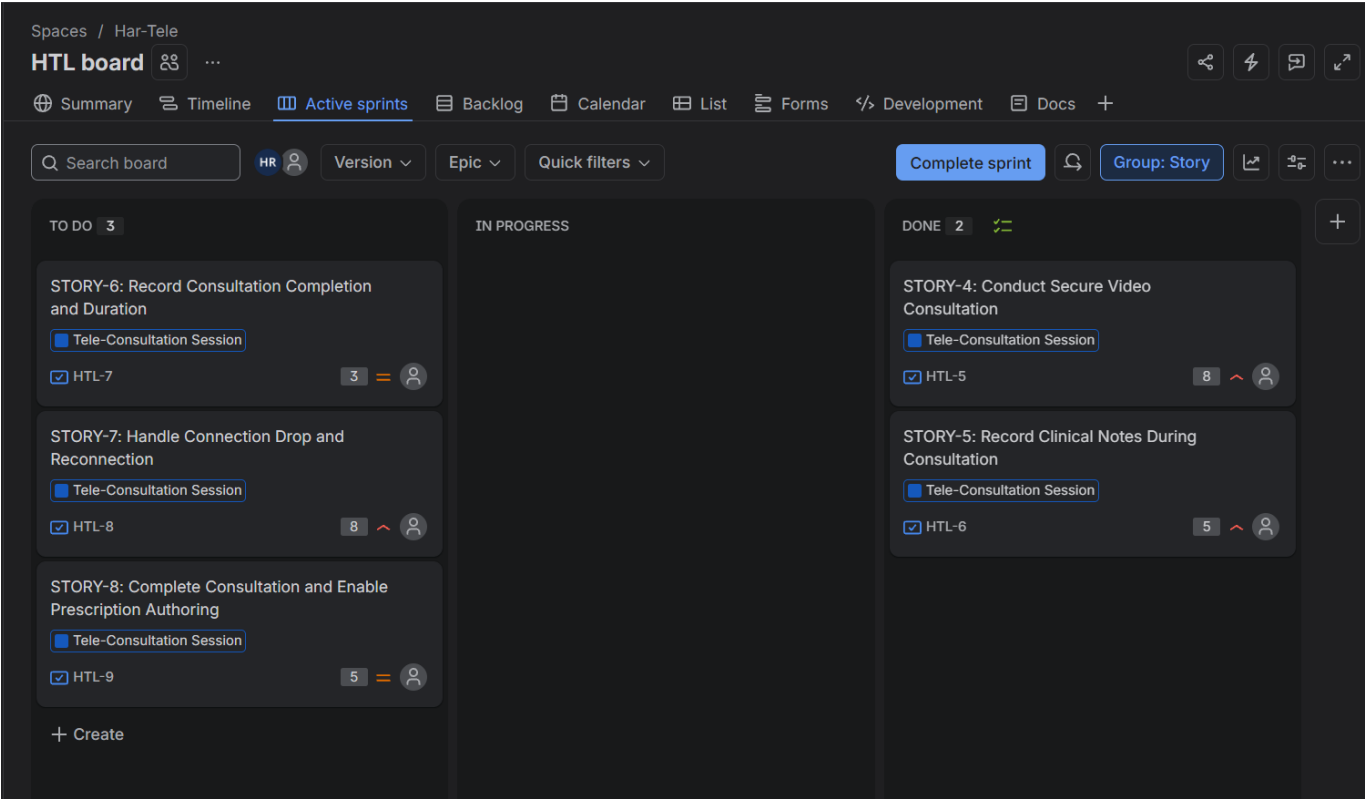


COMPLETED SPRINT-2

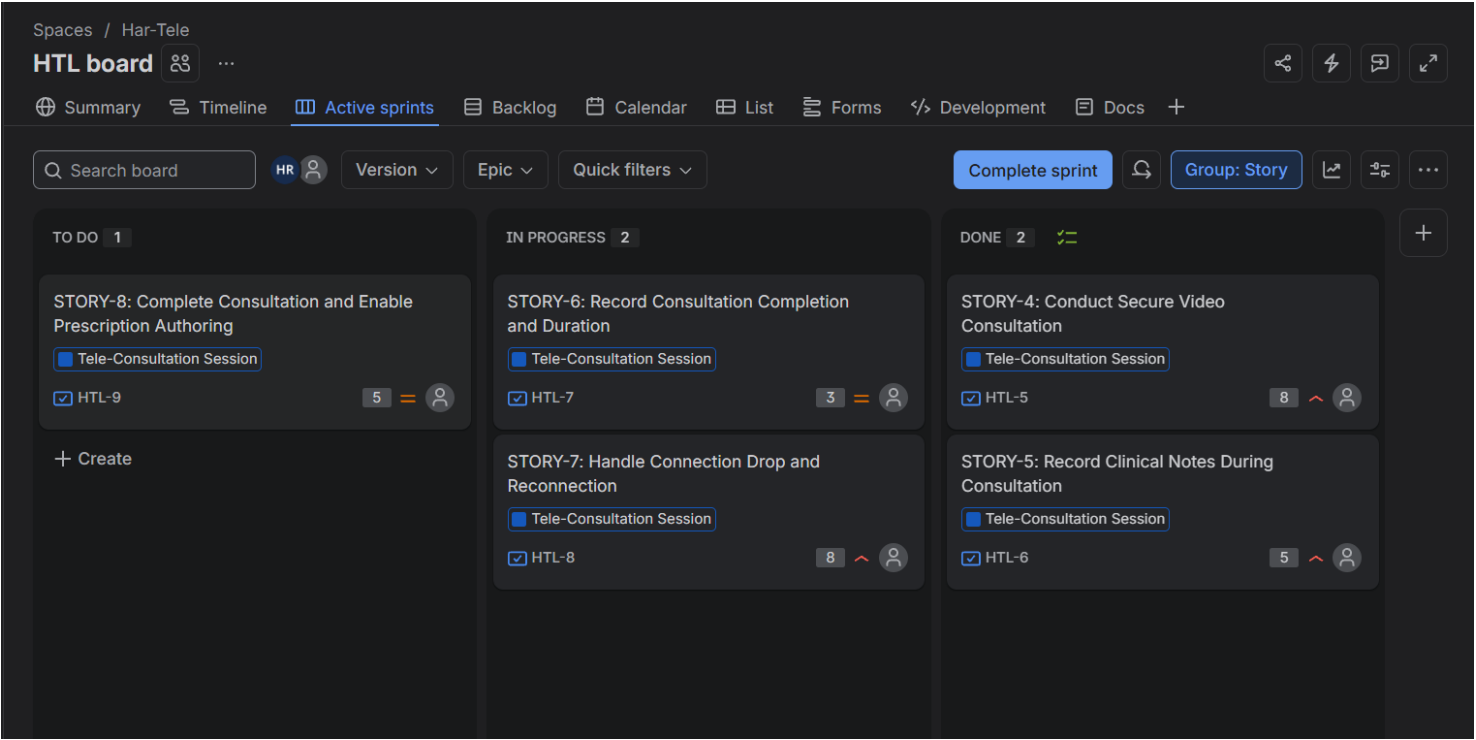


5. Burndown Charts

Both charts use story points. The grey line is the ideal burn rate and the red line is the work left.

BURNDOWN CHART FOR SPRINT-1:

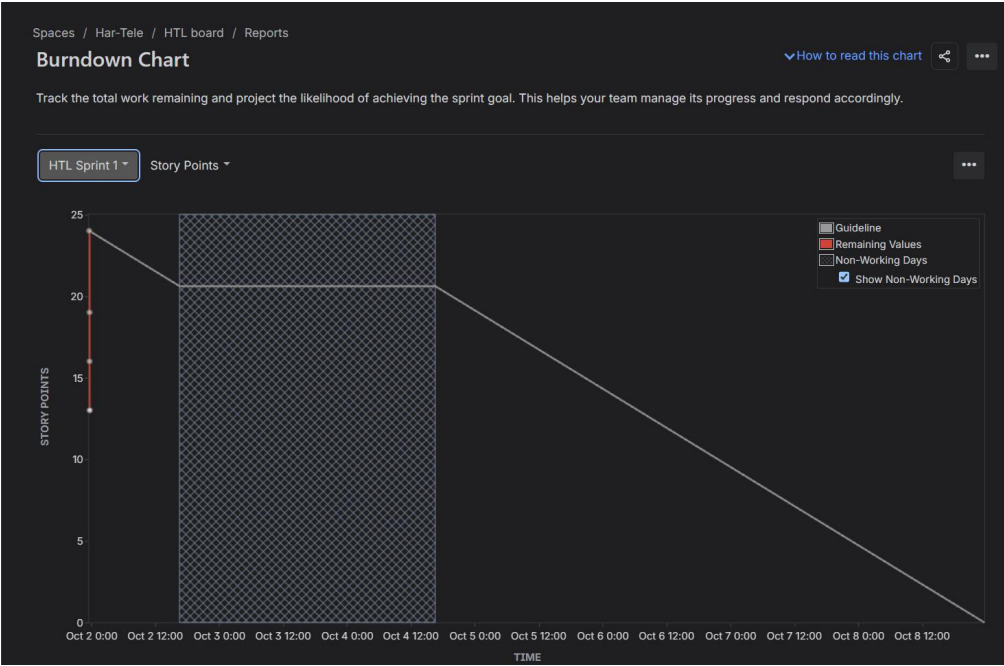

BURNDOWN CHART FOR SPRINT-2:

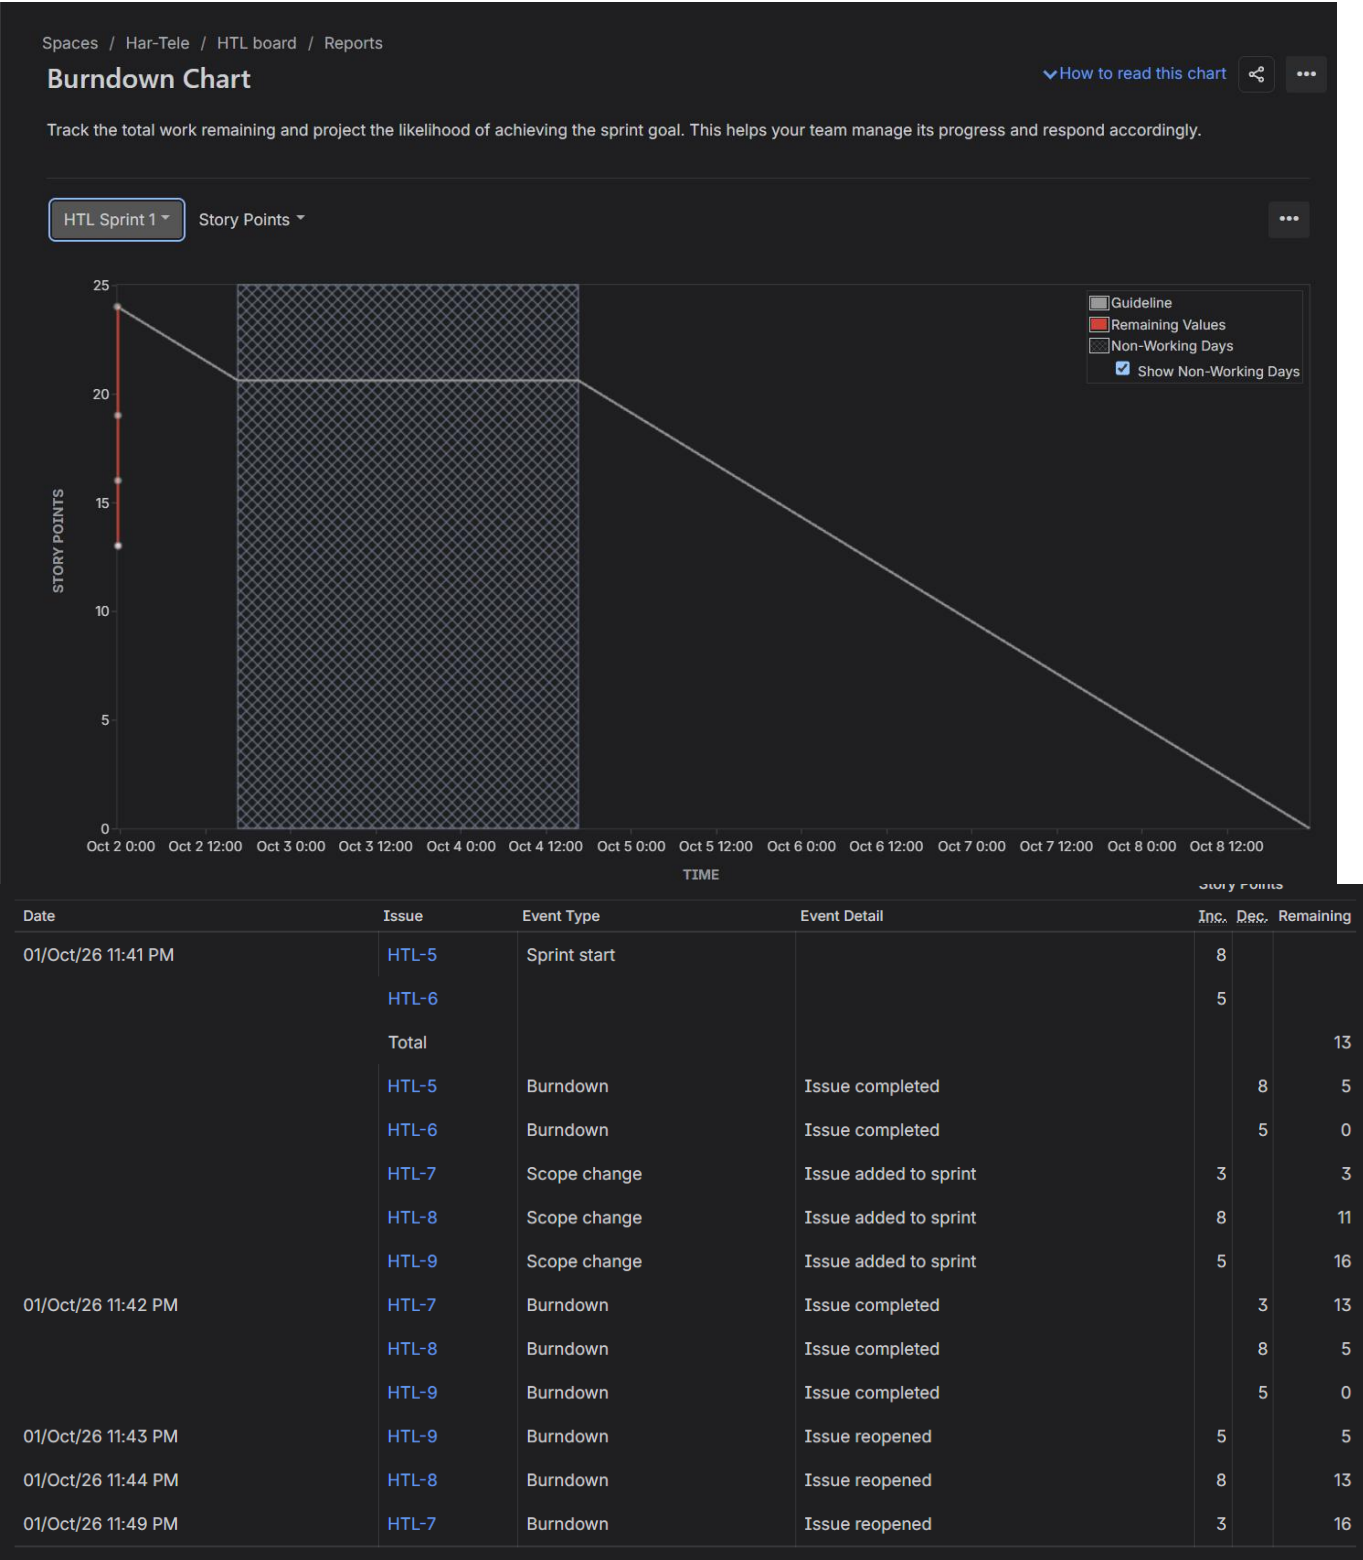

6. Reflection

1. Did your estimations reflect the actual effort?

I can't fully say, because we did not actually build the tele-consultation portal. The work was only simulated by moving the cards across the board, so the actual development effort was not measured. However, the story-

point estimates were based on relative complexity. Smaller tasks such as link validation, waiting-room admission and recording completion were given fewer points, while the secure video consultation and connection-drop/reconnection work received higher points because they involve more states and failure handling. In a real sprint, these larger stories would require more development and testing.

2. Was your backlog well-prioritized?

Mostly. I ordered the stories around the consultation flow: first generate and validate the secure link, then admit the patient, conduct the consultation, record notes, complete the session, handle reconnection, and finally enable the next prescription-authoring step. This follows the dependencies in UC-05, where the consultation includes UC-04 and the consultation must be completed before the next prescription-authoring step. The connection-drop story was given High priority because it handles an important failure scenario.

3. How did your simulated sprint align with your plan?

It matched the plan: Sprint 1 planned 24 points and Sprint 2 planned 16 points, and all planned stories were completed during the simulation. Nothing was carried over and no new stories were added during the sprints. However, this was a controlled simulation where the Jira cards were moved through the workflow, so the result should not be treated as evidence of real development velocity.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts showed how the remaining story points changed as stories were moved to Done. Larger 8-point stories produced larger changes in the remaining work, while smaller stories produced smaller changes. The charts helped show whether the planned work was being completed during each sprint. However, because the sprints were simulated rather than actual development sprints, the charts should not be treated as a real measurement of the team's long-term capacity or velocity.
